

SDC and Office Building Project OFFSITE IMPROVEMENTS

CONSTRUCTION ADVISORY

Week of: Monday June 21, 2010 – Sunday June 27, 2010

Jobsite Location: 14th Ave. S.E. and Jefferson St. S.E.

Project Standard Work Hours: 7:00 a.m. – 5:30 p.m.

Major Work Activities This Week:

- Work will continue to remove and rough grade remaining barrier islands adjacent to the intersection of 14th Ave. S.E. and Jefferson St. S.E.
- Work will begin for installation of new storm water drainage structures and piping. The storm crossing across 14th Ave. S.E. will be installed this week.
- Existing control boxes, signal cabinets, light poles and wiring will be removed for return to the City. New wires will be pulled for connection of street lighting.

Non-Standard Work Hours and Activities:

- Electrical work for removal/re-wiring of equipment and lighting will likely occur on extended shifts during the week.
- Work for installation of storm water drainage structures and piping may occur on Saturday, June 26th, depending on the weather.

Street Closures / Impacts:

- Jefferson Street between 16th Avenue and 14th Avenue will remain closed until the completion of the round-about construction and Jefferson Street improvements currently scheduled to be in mid December 2010.
 - Signed detours remain in place for vehicle as well as bicycle traffic; bicyclists should continue to note that bicycle traffic is not permitted in the 14th Avenue tunnel.
 - Select “No Parking” signs remain in place at Maple Park Drive SE and Jefferson Street SE to safely provide adequate room for buses to make required u-turns during the closure of Jefferson St. SE.
- The intersection of 14th Ave S.E. and Jefferson St S.E. will continue to be controlled by a traffic control officer or set to a flashing mode as necessary during construction activities to help facilitate the flow of vehicle, bicycle and pedestrian traffic. Traffic will be stopped intermittently during work in the roadway. Pedestrians will continue to be flagged through the intersection during construction; bicyclists will be flagged when using crosswalks.
- Please note that traffic revisions shown in the plan for installation of the north storm crossing will remain in place only during working hours, traffic will be restored to the configuration as depicted on the Jefferson St. Road Closure & Detour Plan at night and on weekends.
- **All vehicle, bicycle and pedestrian traffic are reminded to please watch and obey traffic control officers and flaggers.**

NOTES


1. Bicycle detour sign to be placed at trail head.
2. Jefferson St. sidewalks to remain open to pedestrians until further notice. Contractor will need to close sidewalks and detour pedestrians at times for safety.
3. See Detour Plan dated 6/4/2010 for routes during road closure.
4. See Transit 'U-Turn' Plan dated 6/3/2010 for No Parking detail.

DIS Offsite Improvements Project

Traffic Control Plan - St2.0
Jefferson St. Closure

June 4, 2010

Page 1

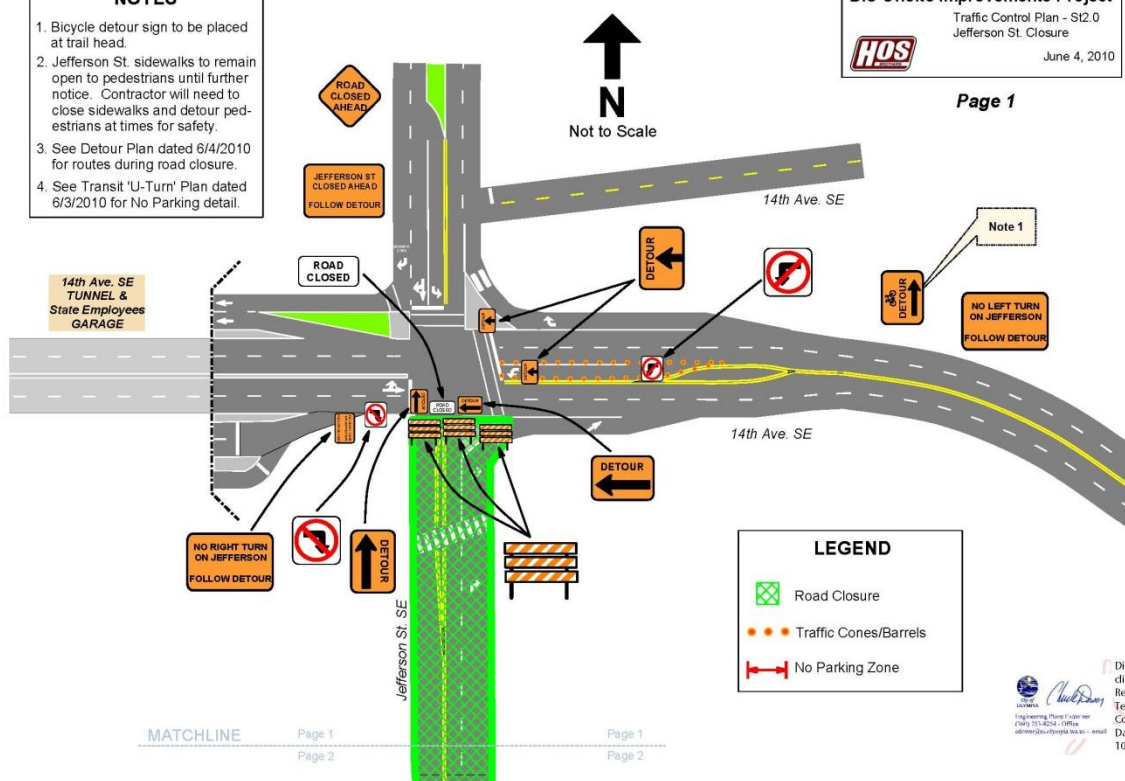

MATCHLINE

Page 1

Page 1

LEGEND

-  Road Closure
-  Traffic Cones/Barrels
-  No Parking Zone

Digitally signed by client2.xohm
Reason: Approved
Temporary Traffic
Control Plan
Date: 2010.06.10
10:38:48 -07'00'

MATCHLINE

Page 1


Page 1

DIS Offsite Improvements Project

Traffic Control Plan - St2.0
Jefferson St. Closure

June 4, 2010

Page 2

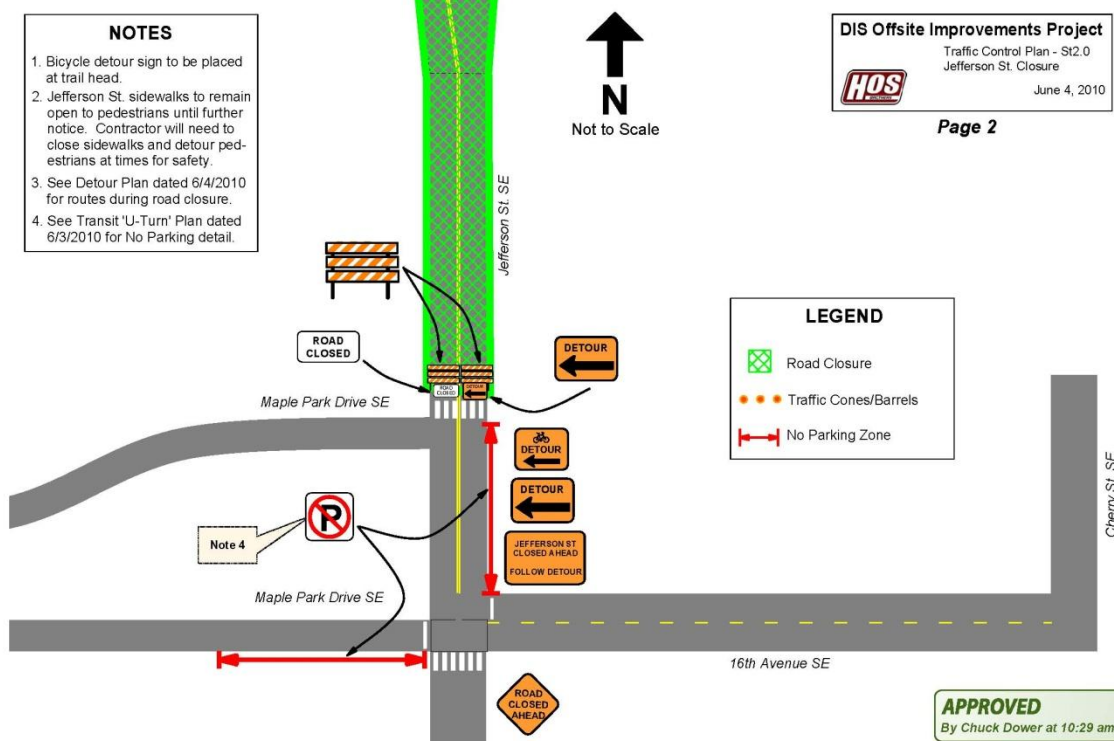

NOTES

1. Bicycle detour sign to be placed at trail head.
2. Jefferson St. sidewalks to remain open to pedestrians until further notice. Contractor will need to close sidewalks and detour pedestrians at times for safety.
3. See Detour Plan dated 6/4/2010 for routes during road closure.
4. See Transit 'U-Turn' Plan dated 6/3/2010 for No Parking detail.

LEGEND

-  Road Closure
-  Traffic Cones/Barrels
-  No Parking Zone

APPROVED

By Chuck Dower at 10:29 am, Jun 10, 2010

NOTES

1. See Road Closure & Detour Plan dated 6/4/2010 for details.
2. Temporary paving (completed in earlier phases).
3. Signs may be placed inside tunnel and/or just outside tunnel's west entrance.
4. Pedestrians to be flagged through intersection during construction. Bicyclists to be flagged when using crosswalks.

DIS Offsite Improvements Project

Traffic Control Plan - St2.1
North Storm Crossing

June 17, 2010

